📅 6-Month Roadmap: Health Tracking App

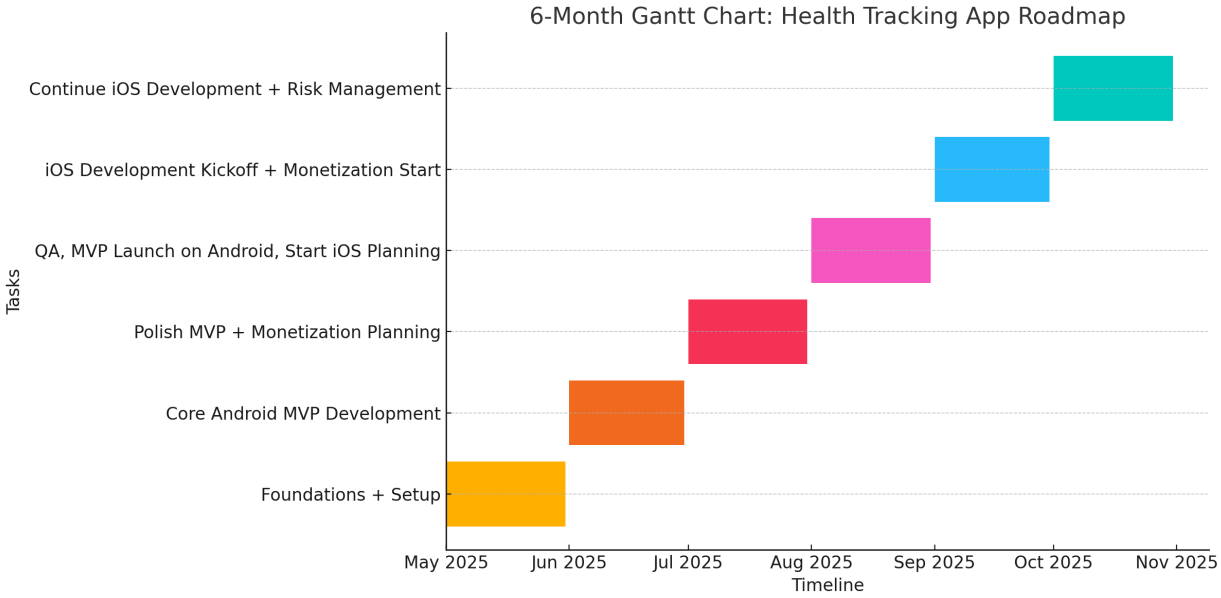

Project Context:

- React Native (Android MVP → then iOS)
- Budget: $30,000
- Team: 4 developers, including design and project management
- **Core Features**
  - Getting data from wearable
  - Showing the data in app with algorithm
  - Triggering alerts
- **Secondary**: Commercialization
  - Users accounts/authentication
  - Data management
  - Monetization
  - Finalization for app store
- Algorithm development, business plan, and legal matters are **out of the development scope.**

Month 1 — Foundations + Setup

Goals:

- Establish core project infrastructure
- Confirm technical feasibility with smartwatch data APIs

Deliverables:

- Finalize feature specs + user flow diagrams
- Set up GitHub repo, CI/CD pipelines, branch strategy
- Setup cloud backend (e.g., Firebase, AWS) for Authentication + Database
- Build basic UI skeleton (login screen, dashboard shell, user account, alert/settings page)
- Start IOT wearable device API integration research & prototyping
- Define database schema for health metrics

Milestones:
✅ Project plans and tech architecture approved
✅ UX/UI Design Done
✅ Successfully retrieve dummy data from Fitbit API

Notes:

- Wearable OAuth/token management must be prioritized early

Month 2 — Core Android MVP Development

Goals:

- Build core user-facing MVP components
- Complete Wearable device integration (real data)

Deliverables:

- Authentication with backend (Email/password or Google sign-in)
- Full IOT wearable device API data sync (heart rate etc.)
- Initial Dashboard page: pull and display user metrics
- Health History log: store and render last 7+ days of metrics
- Implement basic alerts UI and storage of outlier events

Milestones:
✅ Full user login & account creation working
✅ Dashboard populated with real Fitbit data
✅ Health metric history view available

Notes:

- **Potential risk:** Wearable API rate limits or permission scopes

---

Month 3 — Polish MVP + Begin Monetization Planning

Goals:

- Polish experience for Android MVP launch
- Design monetization model

Deliverables:

- Add basic push notification support (possible overdose etc.)
- Refine Dashboard with minor data visualizations (simple charts/graphs)
- Add onboarding tutorial for new users
- Polish UX flows (loading states, error states)
- Implement feature flags: prepare code to separate free vs premium users
- Research and document monetization options:
    - Subscription tier (Pro version)
    - In-app purchase for extra features

Milestones:
✅ MVP feature complete
✅ Monetization plan drafted and feature flags ready

Notes:

- Monetization planning does **NOT** require full implementation yet
- If timeline allows: start simple paywall view for premium upgrade

---

Month 4 — QA, MVP Launch on Android, Start iOS Planning

Goals:

- Finish QA and launch Android MVP
- Start preparing iOS foundations

Deliverables:

- Internal beta testing round (QA, bug fixes)
- External beta (Google Play Beta Test Group)
- Publish Android MVP to Google Play Store
- Collect early user feedback
- Architecture discussions for iOS (how much reuse is possible, e.g., shared backend)

Milestones:
✅ Android MVP launched publicly
✅ iOS tech plan completed

Notes:

- QA and bug fixing should be 2-3 week sprint

(Buffer Month) Month 5 — iOS Development Kickoff + Monetization Start

Goals:

- Begin core iOS app
- Implement monetization for Android

Deliverables:

- Setup iOS app architecture (likely Swift/SwiftUI)
- Basic login/signup flow for iOS
- Integrate Fitbit API on iOS
- Implement actual monetization (subscription screen) in Android app
- In-app purchase or subscription testing (Google Play Console)

Milestones:
✅ iOS development active
✅ Android app updated with premium upgrade option

Notes:

- Prioritize critical Android bug fixes if needed (still support Android)
- Monetization requires Google Play Console setup for payments

---

(Buffer Month) Month 6 — Continue iOS Development + Risk Management

Goals:

- Continue iOS MVP build
- Manage risks related to medical algorithm validation

Deliverables:

- Build iOS Dashboard screen pulling Fitbit data
- Build History log screen on iOS
- Coordinate with medical professionals to review health data outputs
  (Remember: **algorithm accuracy is not developer responsibility**, but coordination may be needed)
- Handle any urgent production issues from Android release (hotfixes)

Milestones:
✅ iOS core features (data fetch, dashboard) complete or near-complete
✅ No critical production issues on Android

Notes:

- Be flexible: if Android production bugs are major, iOS development might slow
- Keep documentation updated for eventual App Store submission

---

Risks & External Dependencies

Dependency	Risk	Mitigation
Fitbit API stability/limits	API quota exhaustion or data field changes	Cache data intelligently; warn users if Fitbit sync is temporarily unavailable
iOS HealthKit access (if later needed)	Apple HealthKit permissions can be complicated	Start with Fitbit-only for MVP, add Apple Watch support in later update
Medical Algorithm Validation	Analysis algorithms could be wrong/misleading	Developers are **NOT** liable for medical validation

Monetization Approval	Google/Apple may reject monetization plans	Follow platform guidelines strictly; start implementation early
Budget Overrun	Unexpected bug fixes or tech debt	Monitor burn rate carefully; use free/low-cost tooling whenever possible

---

Team

Gagan Singh – Technical Program Manager, Microsoft

- Background in product management, AI, and network infrastructure
- Led product on *Mindscape*, an AI app using biometric data for mental health insights
- Experience at Microsoft, Cisco Meraki, and Amazon; blends enterprise and startup experience
  Education: B.S. Informatics & B.A. Business, University of Washington; pursuing M.S. CS, Georgia Tech

Ethan Wang – Full-Stack Developer, TSMC

- Strong in frontend/backend engineering, UI design, and data apps
- Led frontend for *Mindscape*; built .NET systems for TSMC and Hanford cleanup
  Experience in health tech and clean energy sectors
- Education: B.S. Informatics, University of Washington

Viru Repalle – Cybersecurity Researcher, PNNL

- Builds secure software for national critical infrastructure resilience
- Skilled in React, software engineering, and cybersecurity frameworks like C2M2
- Applies secure development across cyber, nuclear, and transmission sectors
- Education: B.S. Informatics, University of Washington; pursuing M.S. Cybersecurity, Georgia Tech

Sachin Dhami – Technical PM & HCI Researcher, Gekko Corporation

- Focus on Human-Computer Interaction and inclusive UX design
  Led development at Gekko Corp; researched generative AI in UX at UW
- Experience across UX research, product, and engineering roles
- Education: B.S. Informatics, University of Washington
